



SEPTEMBER 2026

# FITSTORY

A horizontal orange graphic consisting of a series of small, jagged, upward-pointing lines, similar in style to the OBGOLTS logo.

Requirements, roles, scenarios, modules, MVP scope, wireframes,  
architecture, timeline and budget



PHASE RESULT

# Discovery is complete

Requirements gathered and signed off, roles and their areas of responsibility defined, the user journey mapped, the platform broken into modules, the MVP boundary drawn, wireframes collected for every key screen, the technical architecture designed and the timeline and budget costed.

104

screens in wireframes

49 mobile, 26 web, 29 in team consoles

6

roles

Plus mapping onto the brief list

7

platform modules

Plus the shared core

3

AI features in the MVP

3 more spread across the later phases

≈ 5 mo

MVP scope

5,170 hours of work

≈ 8-9 mo

full build

9,091 hours of work

# Requirements gathered over a series of working calls

| TOPIC                        | WHAT WE COVERED                                                 |
|------------------------------|-----------------------------------------------------------------|
| Kick-off session             | Product, market, business model, expectations of the MVP        |
| Roles and operating model    | Who works in the platform, areas of responsibility, escalations |
| User journey                 | Onboarding, workouts, nutrition, subscription                   |
| Working with a coach         | Chat, calls, nutrition review, supervision                      |
| Monetization and store       | Plans, trial, equipment, delivery                               |
| AI features                  | What the AI does and where its limits lie                       |
| Integrations and health data | Health, app stores, payments, US market requirements            |
| Wireframe review             | Walking the screens, collecting edits                           |
| Final sign-off               | MVP scope, timeline, budget                                     |

The meetings produced working documents: an integration map with a rationale for every service, the scope of the AI features, the technical basis for notifications and alerting, and a breakdown of the Health and Watch integration.

# The platform has six roles

## Client (subscriber)

Mobile app and web · F01-F47, W01-W26

Own profile, workouts, nutrition, chat with a coach, subscription, orders

## Coach

Web console in the full build · T1-T7

Own clients, weekly programs, chats, nutrition reviews, calls, requests to the studio

## Supervisor

Web console · K1-K7

Report queue, client cards, live session monitoring, psych tests, escalations

## Content studio

Web console · S1-S4

Production pipeline, workout metadata, moderation and publishing, food database

## Admin

Web console · A1-A10, S8

Metrics, subscriptions and billing, goods and stock, orders, platform settings, roles and permissions

## Support

Web console · Via the admin console

Client card, payments, technical tickets, temporary access to messages

Access control sits in the database itself rather than in application code: a coach never receives another coach's client, a supervisor cannot see billing, and support cannot read messages without a granted permission.

# 11 permissions across 6 roles

|                           | SUBSCRIBER | COACH   | SUPERVISOR | STUDIO | ADMIN   | SUPPORT  |
|---------------------------|------------|---------|------------|--------|---------|----------|
| Client profile            | full       | partial | partial    |        |         | partial  |
| Workout program           | partial    | full    | partial    |        |         |          |
| Messages                  | full       | partial | on grant   |        |         | on grant |
| Health data               | full       | partial | partial    |        |         |          |
| Nutrition and reviews     | full       | full    | partial    |        |         |          |
| Billing and subscriptions | partial    |         |            |        | full    | partial  |
| Content catalog           | partial    | full    | partial    | full   | full    |          |
| Content publishing        |            |         |            | full   | partial |          |
| Goods and orders          | partial    |         |            |        | full    | partial  |
| Platform settings         |            |         |            |        | full    |          |
| Roles and permissions     |            |         |            |        | full    |          |


66

rules: 11 permissions across 6 roles. In the MVP, policies are written for 5 roles, with an automated test for each permission

Temporary access to messages

Granted by a supervisor for a set term. The client sees a notice and every open is logged

# Client journey from sign-in to a coach

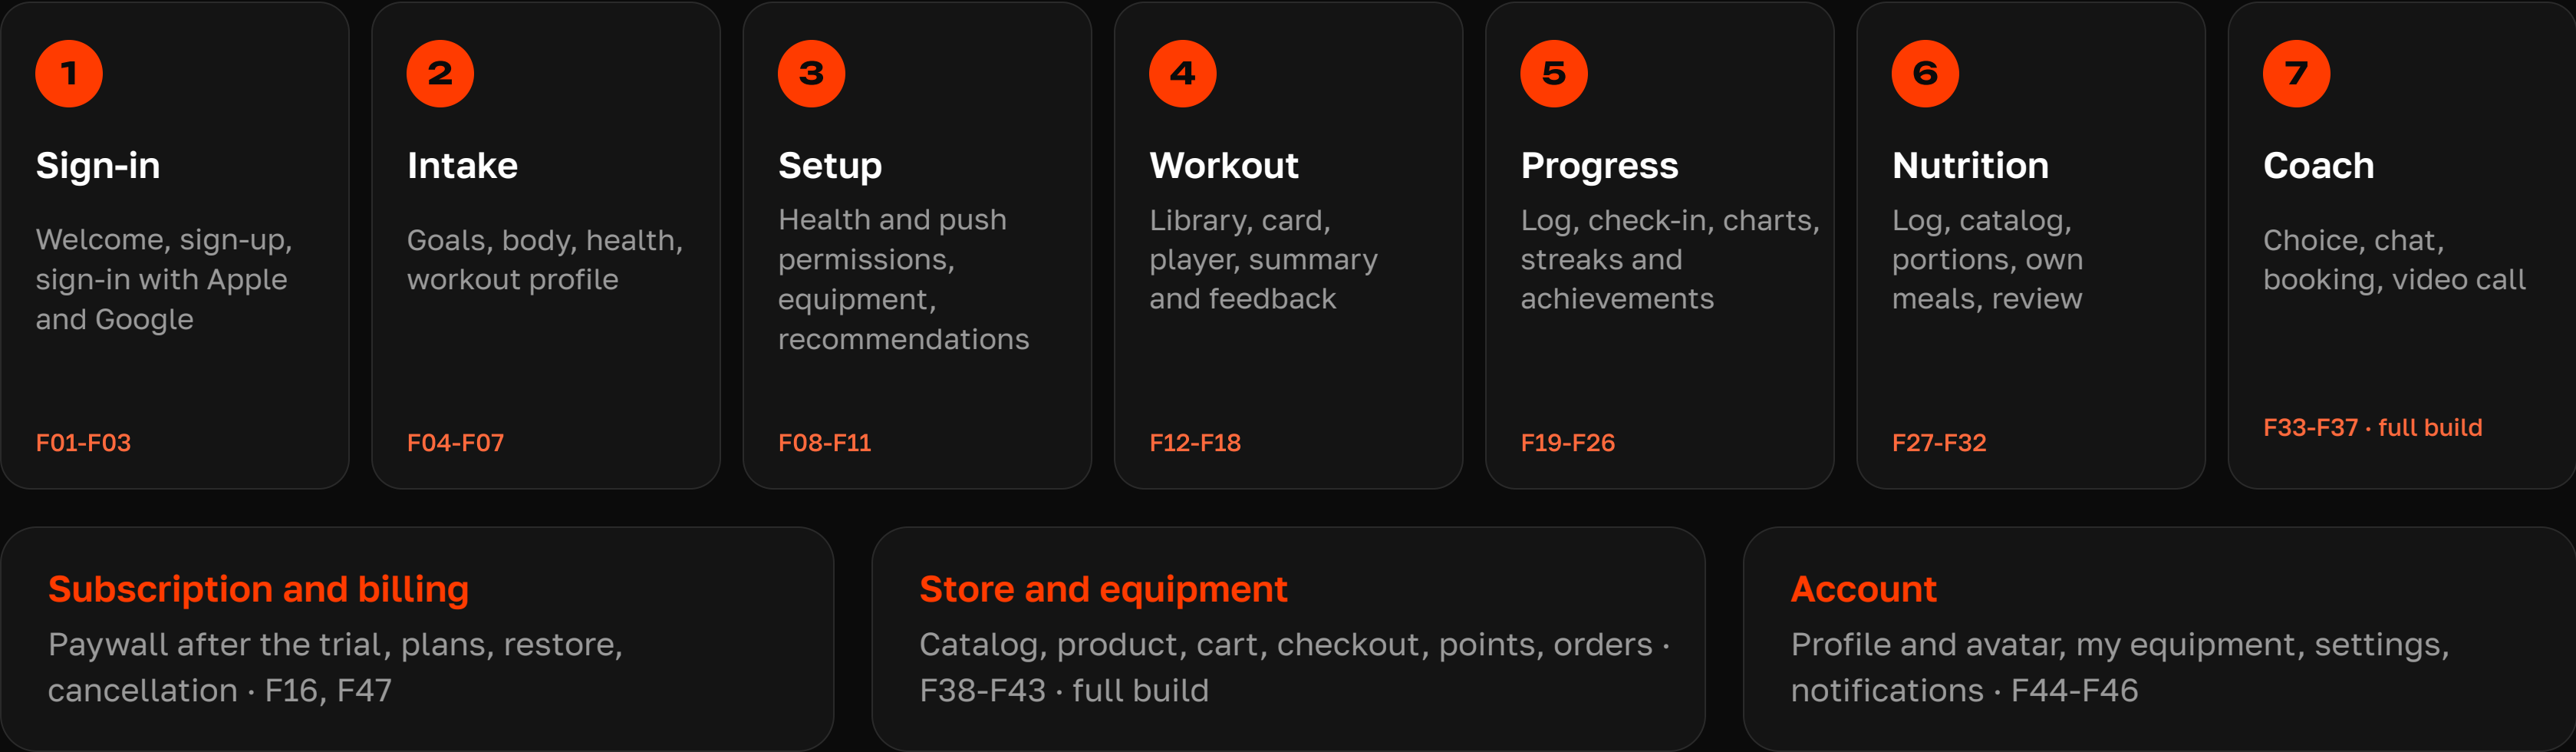


47 screens in the main flow, 2 outside it.

# Ten stages of the client journey in the app and on the web

| Nº | STAGE                | CONTENTS                                                                            | MOBILE   | WEB          |
|----|----------------------|-------------------------------------------------------------------------------------|----------|--------------|
| 1  | Sign-in              | Welcome, sign-up, sign-in with Apple and Google                                     | F01-F03  | W01          |
| 2  | Intake               | Goals, body metrics, health and limitations, workout profile                        | F04-F07  | W01-W02      |
| 3  | Setup                | Health and notification permissions, equipment, thank-you and coach recommendations | F08-F11  | W03, W06-W07 |
| 4  | First workout        | Library, card, phased player, strength block, summary and feedback                  | F12-F18  | W08-W10      |
| 5  | Progress             | Workout log, daily check-in, charts, strength, challenges, before and after         | F19-F26  | W18, W22     |
| 6  | Nutrition            | Log, catalog and search, product card, own meal, coach review                       | F27-F32  | W19-W21      |
| 7  | Working with a coach | Choosing a coach, card, chat, booking, video call                                   | F33-F37  | W13-W17      |
| 8  | Subscription         | Paywall after the trial, plans, cancellation                                        | F16, F47 | W11          |
| 9  | Store                | Catalog, product, cart, checkout, points, orders                                    | F38-F43  | W24          |
| 10 | Account              | Profile and avatar, my equipment, settings                                          | F44-F46  | W25-W26      |

Alongside the main journey we documented the operational role scenarios: a supervisor working the report queue, a coach running the week’s program, the studio producing and moderating content, and an admin working with metrics, stock and orders.

# Seven platform modules and a shared core

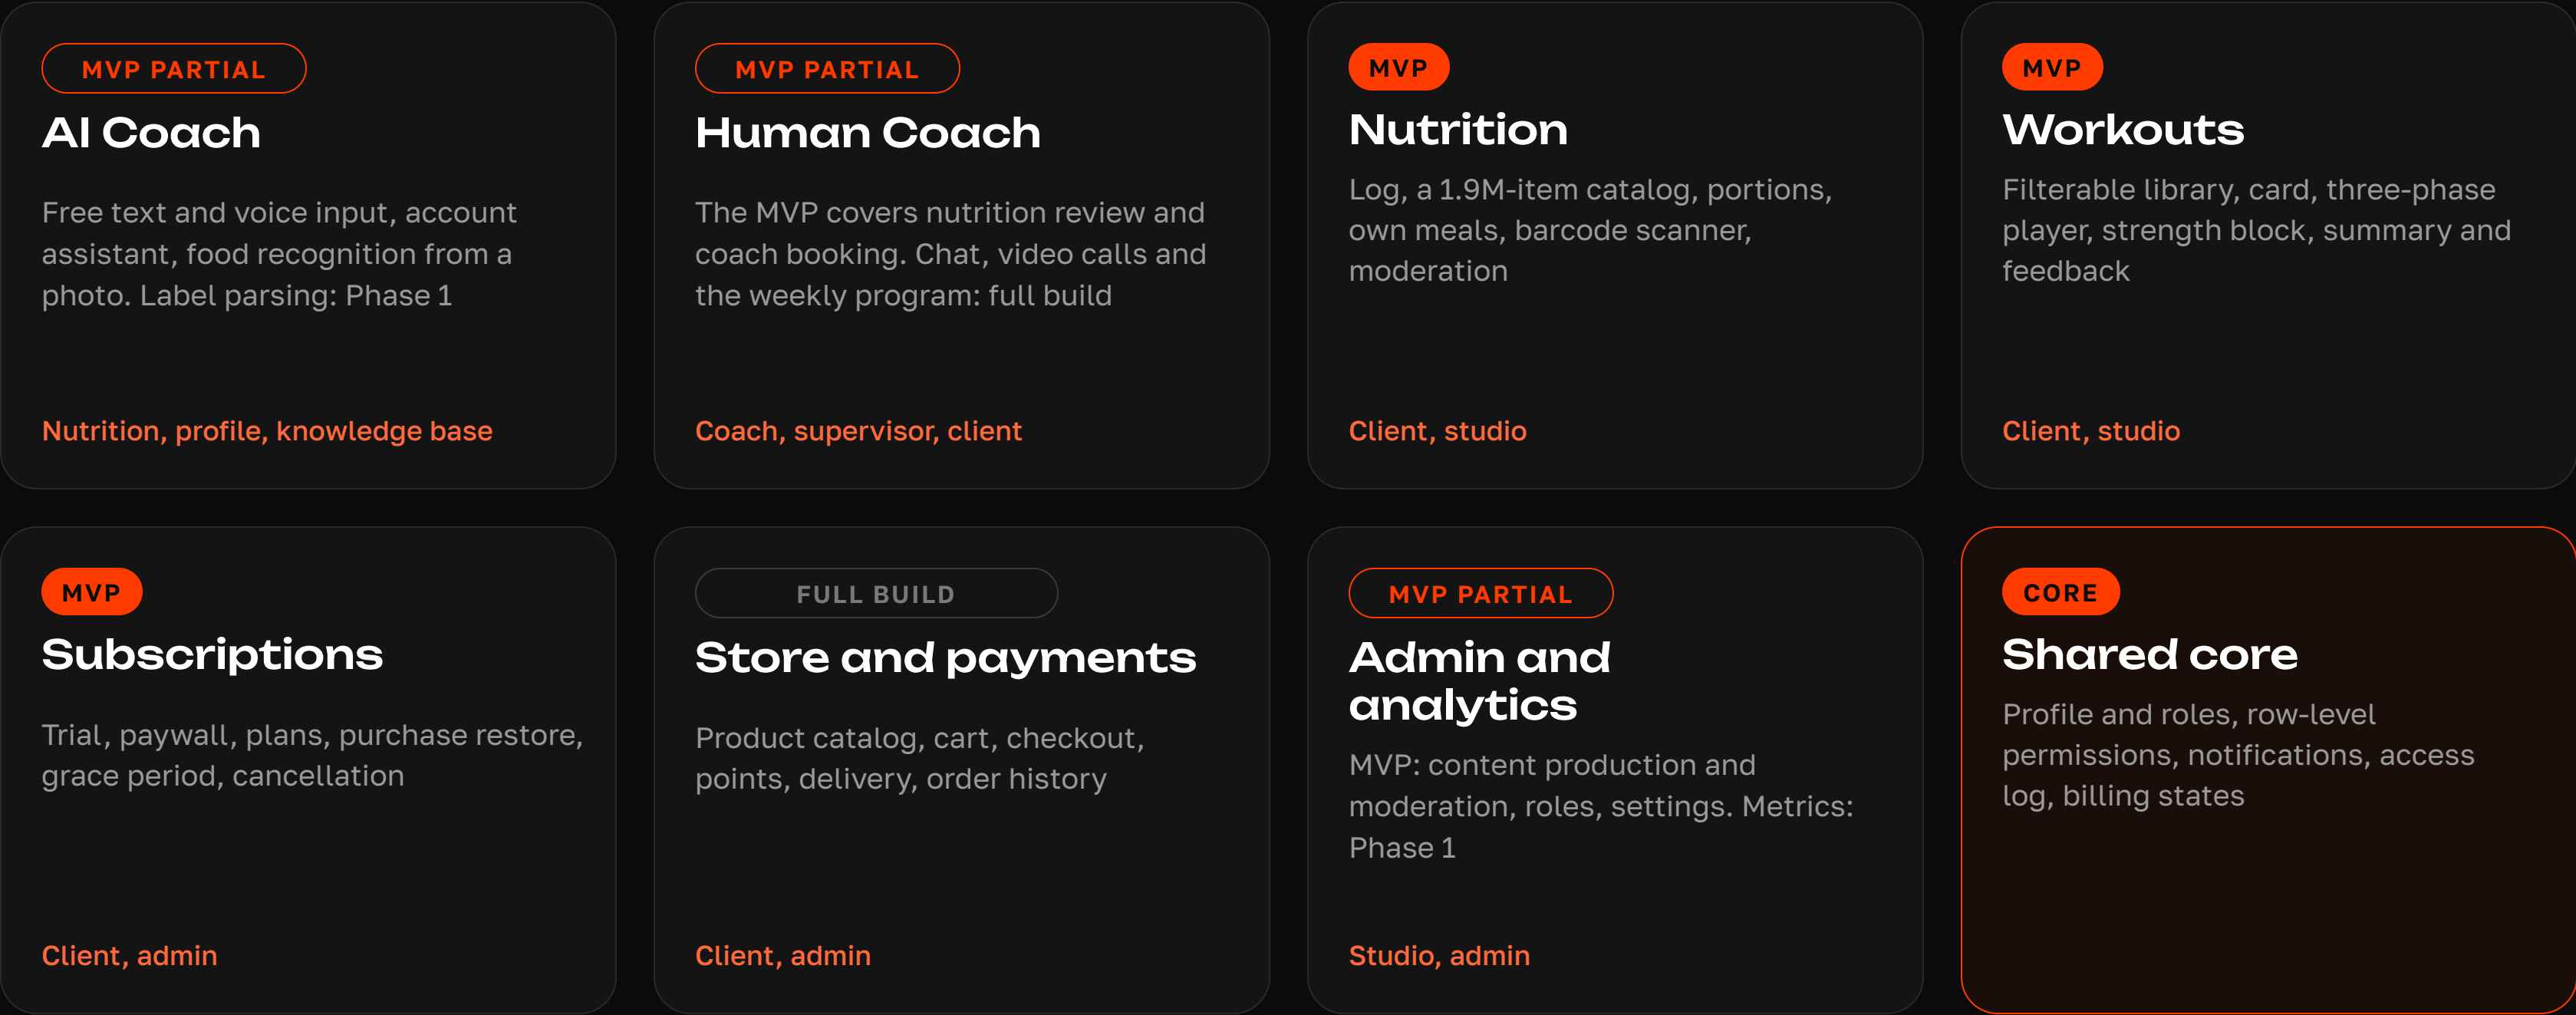

# What is in the MVP and what is deferred

| BLOCK                                 | MVP | PHASE 1 | FULL |
|---------------------------------------|-----|---------|------|
| Onboarding and intake                 | ●   | ●       | ●    |
| Workouts and player                   | ●   | ●       | ●    |
| Nutrition and food catalog            | ●   | ●       | ●    |
| Check-in and progress                 | ●   | ●       | ●    |
| Subscription and paywall              | ●   | ●       | ●    |
| Supervisor, studio and admin consoles | ●   | ●       | ●    |
| AI: free input and assistant          | ●   | ●       | ●    |
| AI: food recognition from a photo     | ●   | ●       | ●    |
| AI result preview from a photo        | ●   | ●       | ●    |
| AI: label parsing                     | —   | ●       | ●    |
| Strength log                          | —   | ●       | ●    |
| Health sync                           | —   | ●       | ●    |
| Product analytics and dashboards      | —   | ●       | ●    |
| Client web version, 26 screens        | —   | —       | ●    |
| Chat and calls with a coach           | —   | —       | ●    |
| Equipment store and delivery          | —   | —       | ●    |
| Full coach console                    | —   | —       | ●    |

# Three AI features in the MVP

MVP

## Free text and voice input

A phrase like “had borscht, two eggs and coffee with milk” is broken into catalog items with portions

WHAT IT RUNS ON

Food catalog, parsing model

EFFECT

Removes half the taps in the log

MVP

## AI account assistant

Answers questions about the schedule, the subscription and plan changes from account data and the knowledge base

WHAT IT RUNS ON

Profile, subscription, plan, article base

LIMIT

No health advice; anything contentious goes to a human

MVP

## Food recognition from a photo

A photo of a plate becomes items with gram weights and the user edits the draft

WHAT IT RUNS ON

An off-the-shelf recognition service or a multimodal model

IN THE MVP

A list, with no overlay on the photo. The result is always a draft

Label parsing is deferred to Phase 1: by then there will be real data on what people enter and how.


# Six AI features by phase

| FEATURE                        | WHAT IT DOES                                               | PHASE   | LIMIT                                      |
|--------------------------------|------------------------------------------------------------|---------|--------------------------------------------|
| Free text and voice input      | A phrase is broken into catalog items with portions        | MVP     | Removes half the taps in the log           |
| AI account assistant           | Answers on schedule, subscription and plan changes         | MVP     | No health advice                           |
| Food recognition from a photo  | A photo of a plate becomes items with gram weights         | MVP     | The result is always a draft               |
| AI result preview from a photo | Predicts appearance after the goal is reached              | MVP     | Needs separate work on ethics and accuracy |
| Label parsing                  | A photo of the label becomes a draft product card          | PHASE 1 | Closes the “app does not know my food” gap |
| Message tone personalization   | Tunes notifications and weekly summaries to the psych test | PHASE 1 | Templates need moderation                  |

A recognition result always stays a draft that the user confirms. The assistant gives no health or nutrition advice and hands any contentious question to a human. In the team consoles, AI flags contentious photos and merges duplicate meals in the food database.


# Wireframes collected for every key screen

| BLOCK                        | SCREENS | NUMBERING  | CONTENTS                                                               |
|------------------------------|---------|------------|------------------------------------------------------------------------|
| Mobile app, main flow        | 47      | F01-F47    | The full path from welcome to cancellation                             |
| Mobile app, outside the flow | 2       | M08, M10   | AI preview, pre-trial carousel                                         |
| Client web version           | 26      | W01-W26    | Onboarding, workouts, nutrition, progress, store, profile              |
| Coach console                | 7       | T1-T7      | Clients, weekly program, chats, schedule, nutrition, requests, dossier |
| Supervisor console           | 7       | K1-K7      | Report queue, client card, live monitoring, psych tests, escalations   |
| Content studio               | 4       | S1-S4      | Pipeline, metadata, moderation, food database                          |
| Admin console                | 11      | A1-A10, S8 | Metrics, funnels, billing, coaches, store, stock, orders, roles        |
| Total                        | 104     |            |                                                                        |



Layout, block structure, transitions and logic, without the final visual design. The mockups are built in layers rather than as images, so they go straight into design with no rebuild.

# Clients, the platform core and external services

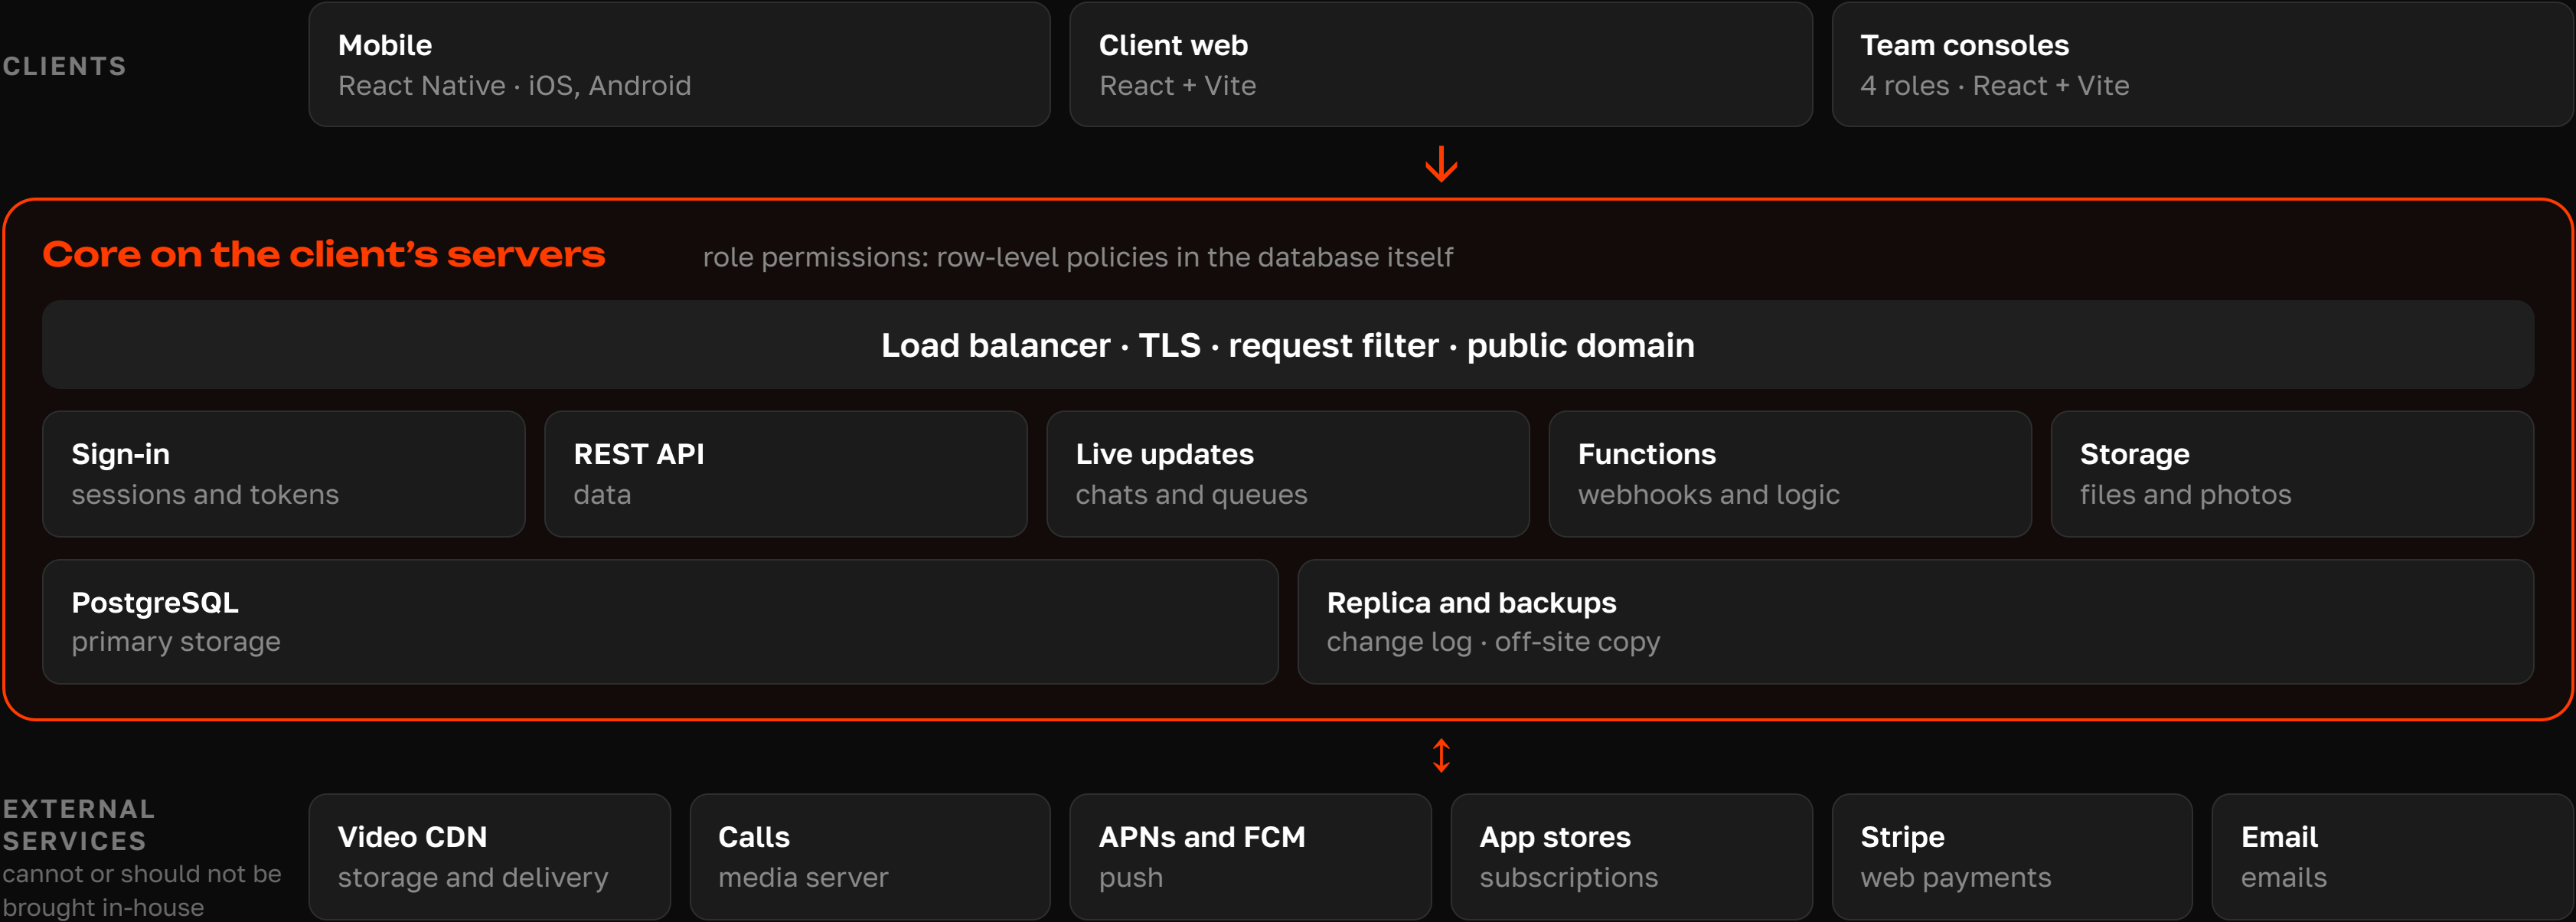

# The core is deployed on the client's own dedicated servers

## Clients

The mobile app is React Native, one codebase for iOS and Android. The client web version and the team consoles are React and Vite, all in a single repository: business logic and the API client are reused, and only the presentation layer differs.

## Core

Open-source components inside one perimeter on the client's dedicated servers: PostgreSQL, a sign-in and session service, a REST generator over the schema, live updates, object storage and a serverless function runtime. Only what cannot be moved stays outside: notifications, app stores, payments, video and calls.

## Why our own servers

The platform handles health metrics, and in the US that means:

### Washington My Health My Data

with a private right of action


### CCPA and CPRA

### Illinois BIPA


for photographs

Health data never leaves the client's perimeter, and every access to it is written to the log.

# Four zones with one-way traffic

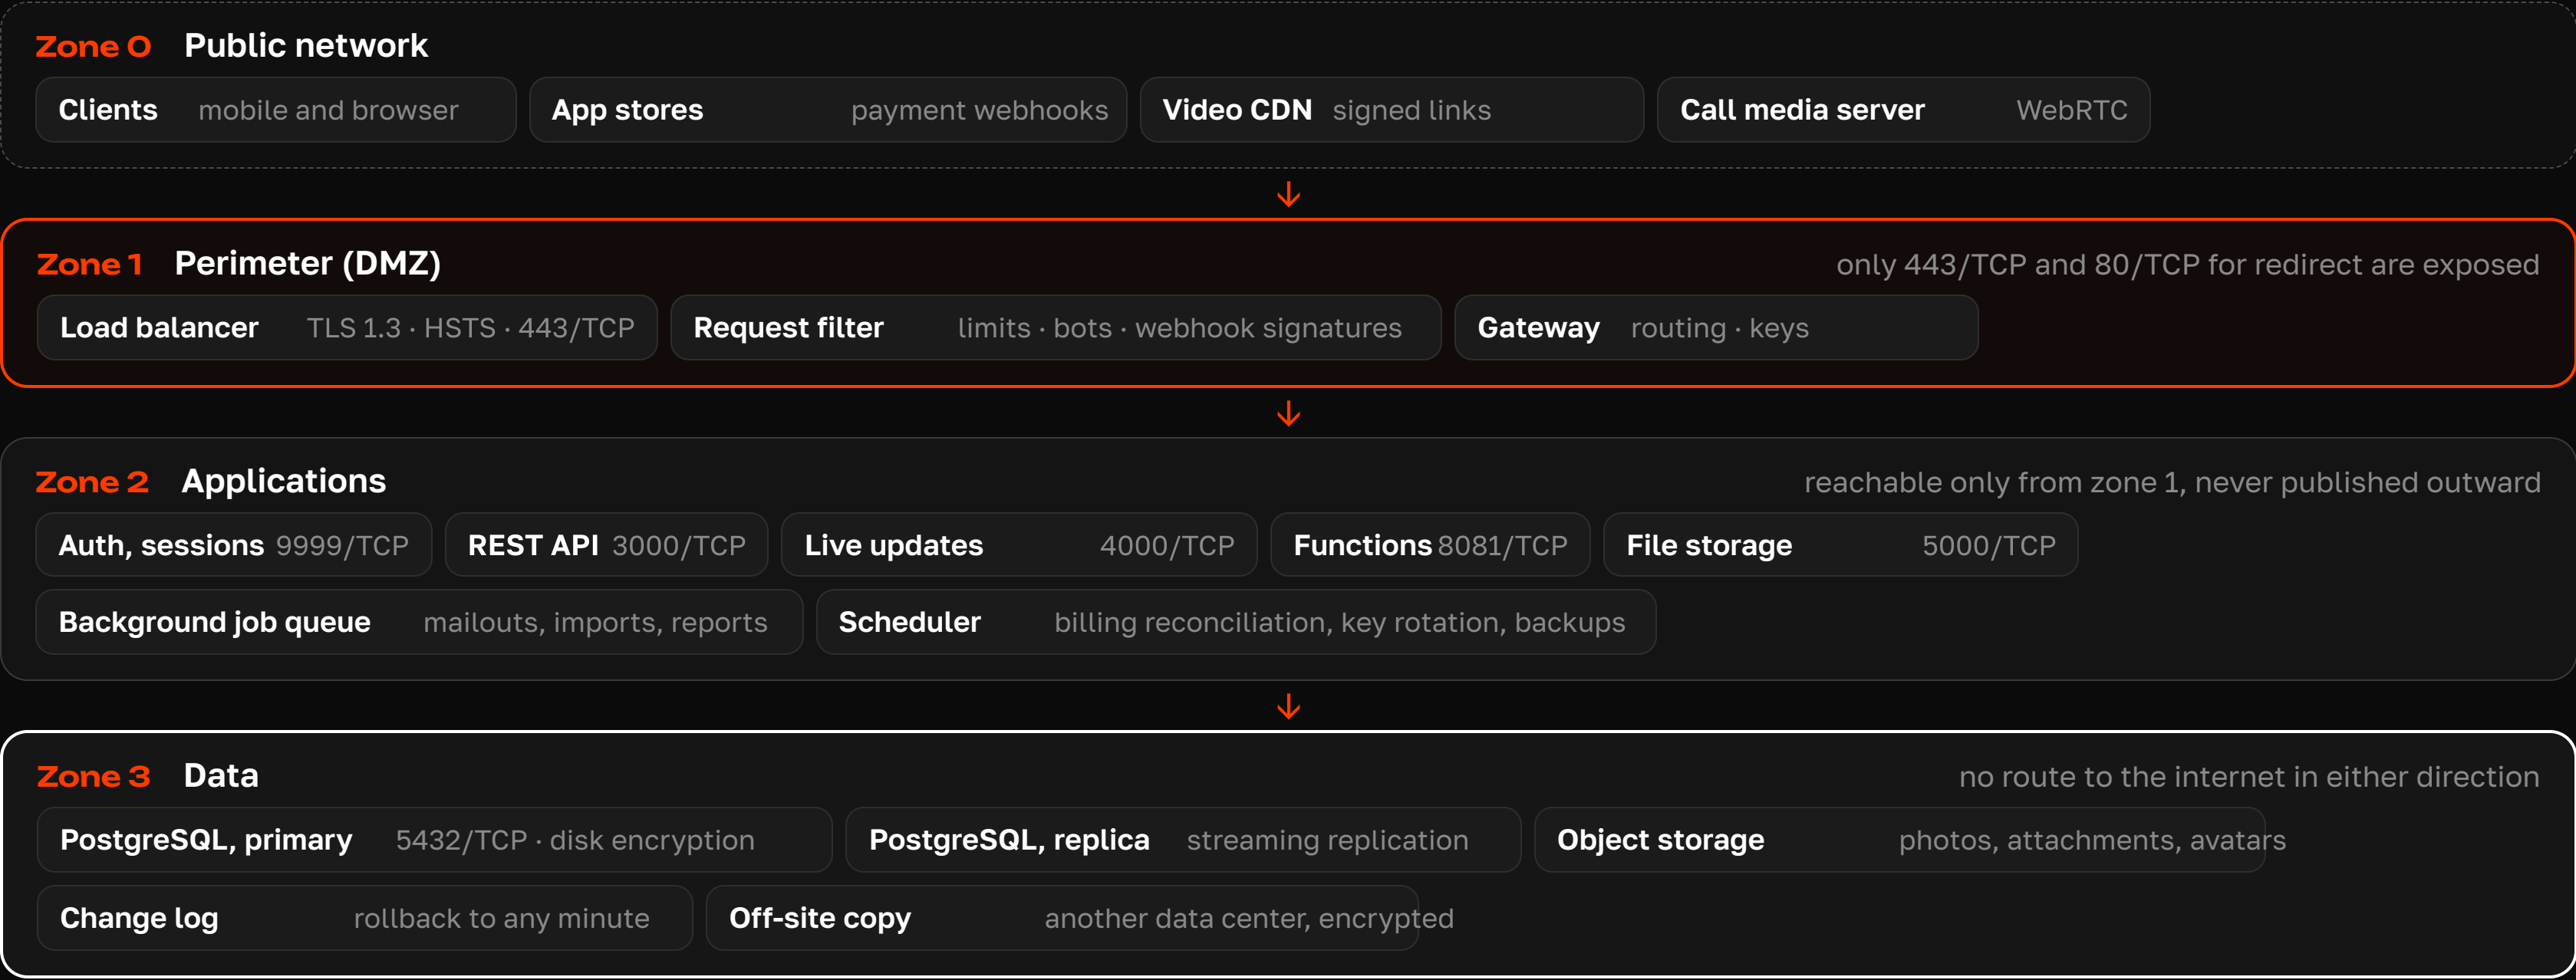

# Not a single medical record leaves the perimeter

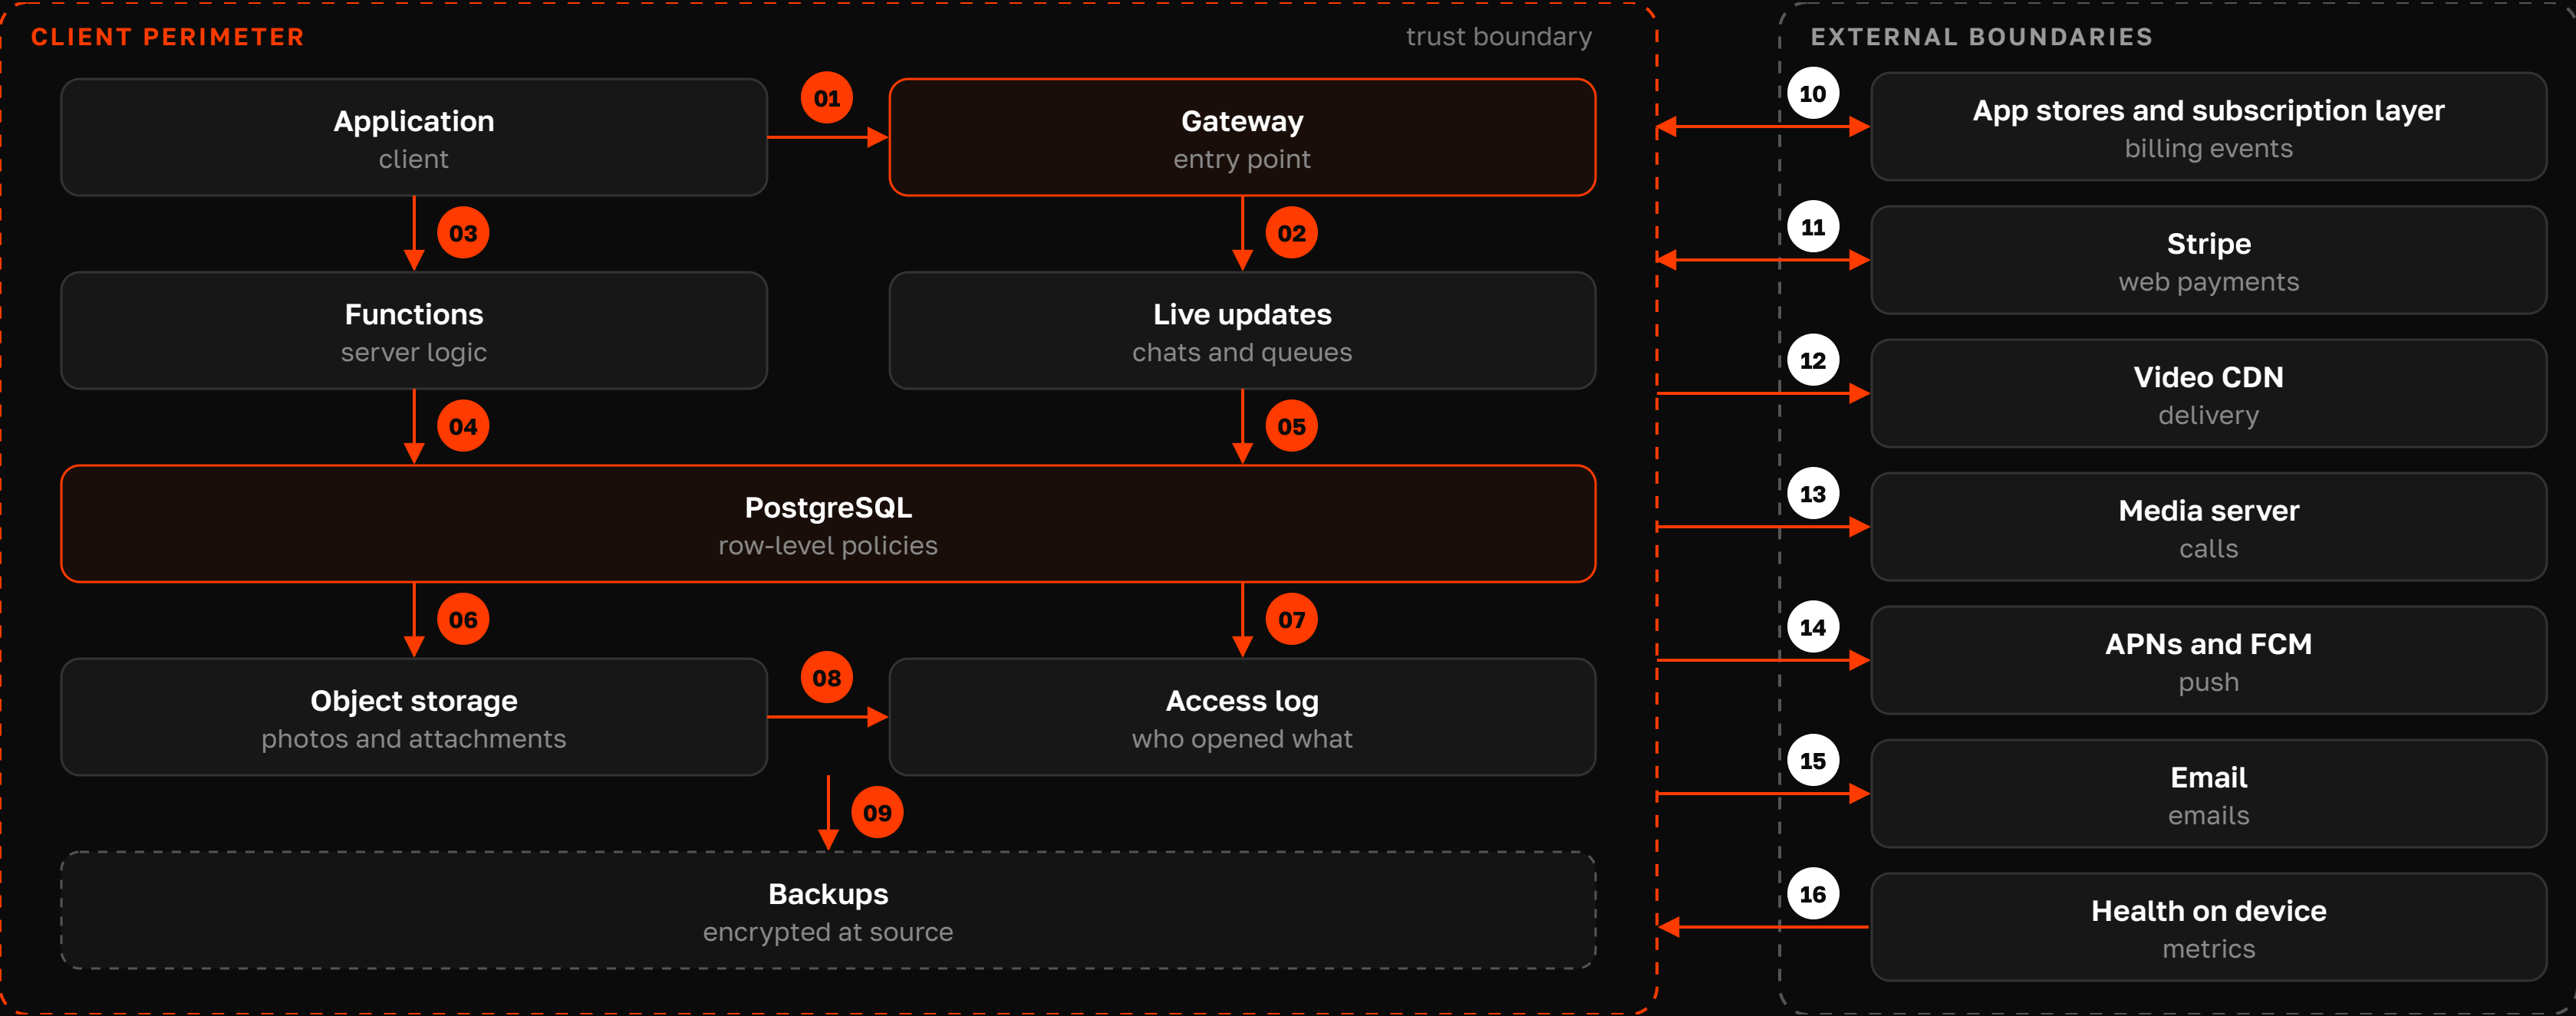


# Two servers and space for backups are enough at launch

| NODE               | START                       | WHAT RUNS ON IT                       | GROWTH                               |
|--------------------|-----------------------------|---------------------------------------|--------------------------------------|
| Application server | 8 cores, 16 GB, 200 GB NVMe | Load balancer, gateway, core services | 2 nodes behind the balancer          |
| Database server    | 8 cores, 32 GB, 500 GB NVMe | PostgreSQL and object storage         | 16 cores, 64 GB, 1 TB plus a replica |
| Backup storage     | 2 TB, S3-compatible         | Daily snapshot and change log         | 4 TB, another data center            |


A high-availability setup adds a second application server, a hot database replica and a separate node for files. Server rental and the work on deployment, high availability, monitoring and operating procedures are included in the project cost.

# Three releases

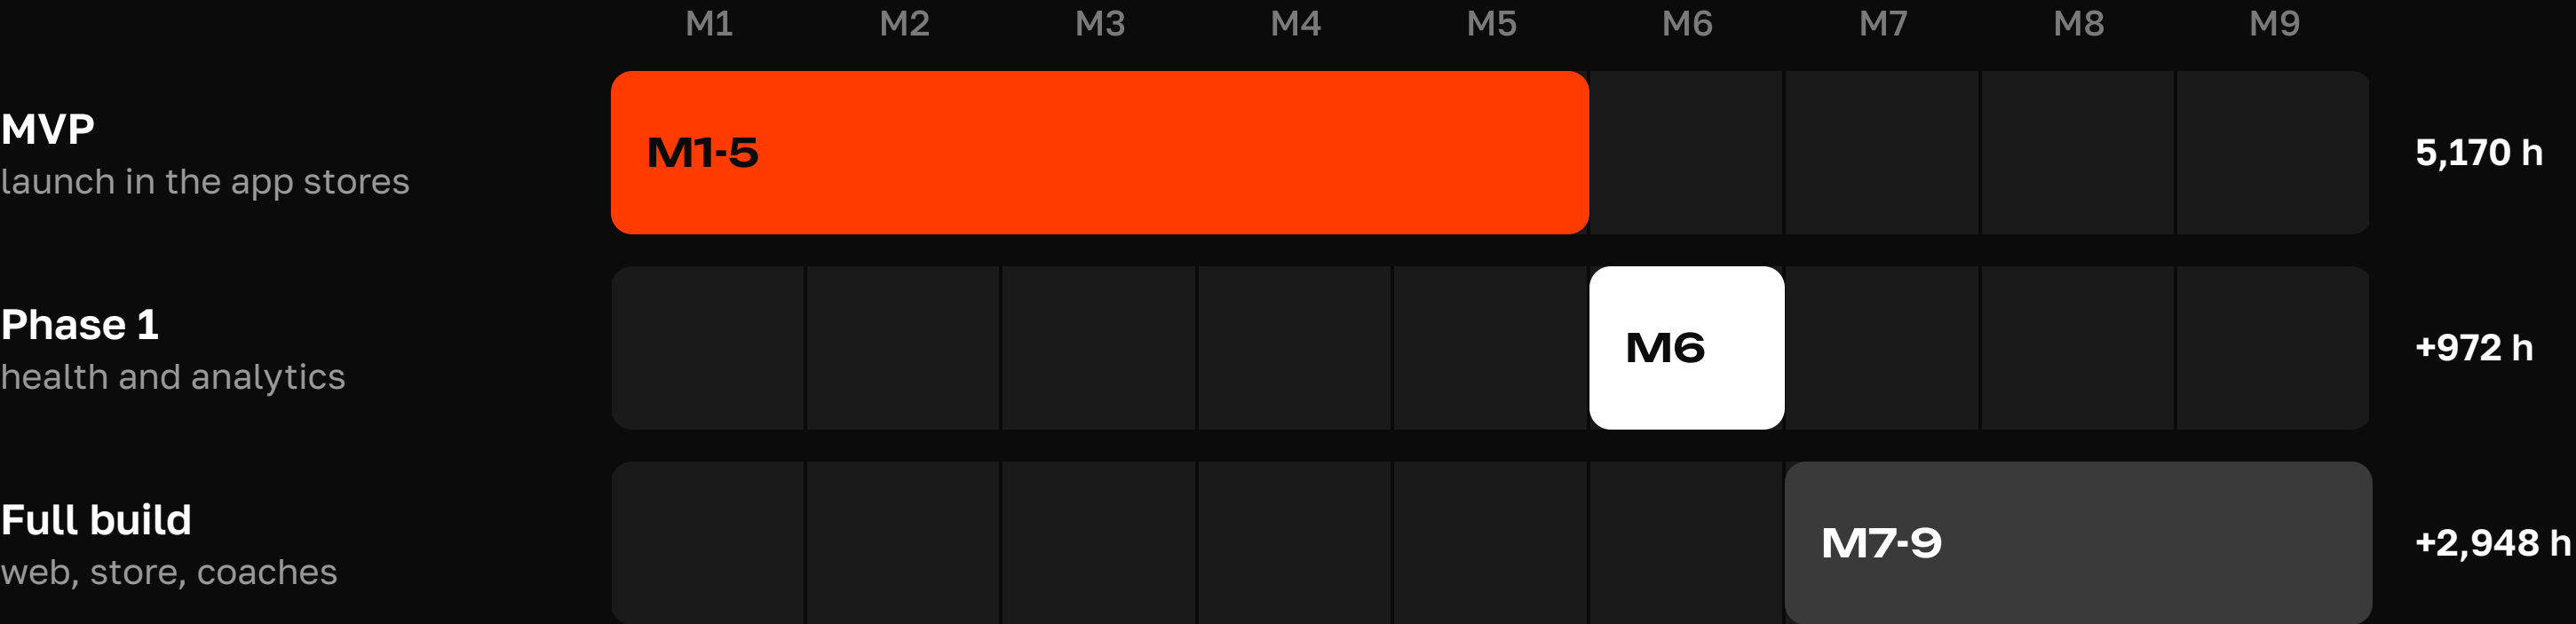

The timeline assumes a team of 2 backend, 2 React Native, 1 React, 1 QA, a designer and a manager. A second React developer on the full build cuts roughly a month off the schedule.

# Three estimates

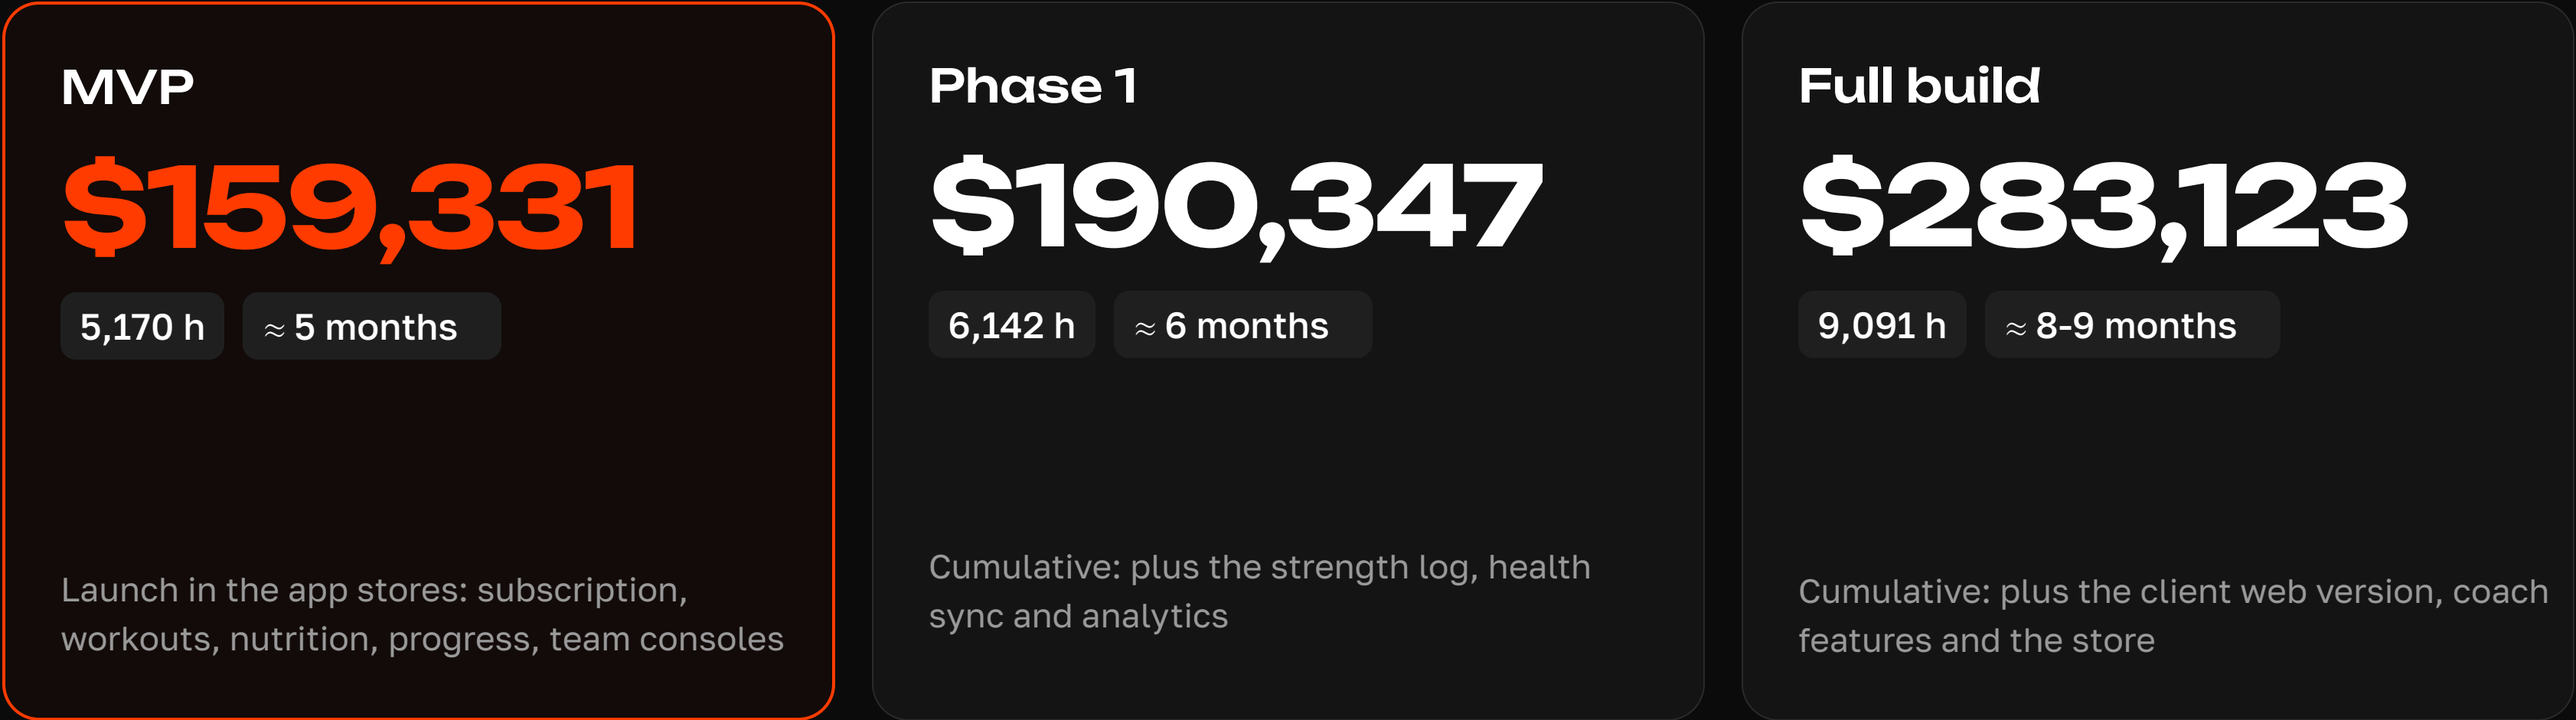

Phase 1 and the full build are shown cumulatively: this is the cost of the whole project at that scope, not a top-up on the previous stage.

# Budget by role for each estimate

| ROLE            | \$/H | MVP, H  | MVP, \$   | PHASE 1, H | PHASE 1, \$ | FULL, H | FULL, \$  |
|-----------------|------|---------|-----------|------------|-------------|---------|-----------|
| Design          | 13.2 | 269.6   | \$3,559   | 330        | \$4,356     | 533     | \$7,036   |
| Backend         | 35   | 1,545.5 | \$54,093  | 1,762      | \$61,670    | 2,599.5 | \$90,983  |
| React Native    | 30   | 1,552.3 | \$46,569  | 1,764      | \$52,920    | 2,546   | \$76,380  |
| React, consoles | 35   | 712     | \$24,920  | 900        | \$31,500    | 1,400   | \$49,000  |
| AI              | 50   | 208     | \$10,400  | 309        | \$15,450    | 471     | \$23,550  |
| QA              | 15   | 360.1   | \$5,402   | 420        | \$6,300     | 520     | \$7,800   |
| Management      | 35   | 291.6   | \$10,000  | 354.1      | \$12,394    | 561     | \$19,635  |
| Marketing       | 19   | 231     | \$4,389   | 303        | \$5,757     | 460     | \$8,740   |
| Total           |      | 5,170.1 | \$159,331 | 6,142.1    | \$190,347   | 9,090.5 | \$283,123 |

Amounts in US dollars, rounded to whole units.

# What is not in the budget

- |           |                             |                                                                          |
|-----------|-----------------------------|--------------------------------------------------------------------------|
| <b>01</b> | <b>Third-party services</b> | Video, calls, email, analytics, monitoring: from \$285 a month at launch |
| <b>02</b> | <b>One-off payments</b>     | Apple Developer Program \$99 a year, Google Play Console \$25            |

## Already included in the project cost

Server rental, infrastructure deployment, high availability, monitoring and operating procedures, fees

OBGOLTS  
edia Group

—darkfactory

FITSTORY · SEPTEMBER 2026
